

Progress Report
MCN Build, Inc.
4/25/23

Maret Athletics Field 5901 Utah Ave NW Washington, DC 20015





I. Four Week Review, Lookahead & Complaints, Questions and Concerns

Four Week Review

- Mobilization of tree transplant crews
- Received SCE Permit 10988027 Construction entrance permit
 - o Permit includes traffic control plan for Nebraska Ave. for entry and exit of equipment trucks
- Trenched out four heritage trees in preparation for transplant
- Dug exit ramp for first two heritage tree transplants
- Completed engineering stakeouts for final locations of transplanted heritage trees
- Placed first heritage tree in its new location in the northeast corner of the site and backfilled previous location of tree #1
- Placed second heritage tree in its new location in the northwest corner of the site
- Completed repair of neighbor's retaining wall at 5833 Nebraska
- Periodic inspection visits from MCN site safety supervisor

Lookahead

- Continue transplanting trees as designated on tree transplant plan
 - o Transplant Week 1 Mobilization and Stormwater Pollution Prevention Plan COMPLETE
 - Transplant Week 2 Encapsulate root balls of all four trees and install piping under root balls of trees 1 and 2 TREE 1 COMPLETE AND TREE 2 IN PROGRESS
 - Transplant Week 3 Install the structural frame to support the transplants of trees 1 and 2 TREE
 1 COMPLETE AND TREE 2 IN PROGRESS
 - Transplant Week 4 Transplant trees 1 and 2 and backfill and dress the two trees TREE 1 COMPLETE; TREE 2 COMPLETE
 - o Transplant Week 5 Install piping under root balls of trees 3 and 4 and install structural frame to support the transplants of trees 3 and 4 − **IN PROGRESS**
 - o Transplant Week 6 Transplant trees 3 and 4 and backfill and dress the two trees **IN PROGRESS**
 - Transplant Week 7 Complete final grading around trees, install irrigation and mulch and demobilize equipment
- Continue to water trees in advance of transplant and after transplant
- Install irrigation pump for transplanted trees
- Install irrigation system for transplanted trees
- Continued inspection from MCN site safety supervisor

Complaints, Questions, and Concerns

- On April 5 a neighbor reported construction activity on the site at 6:46am and provided video of a backhoe loader moving materials on the site
 - o MCN site supervisor made it clear to the team working that the prohibition on construction activity included relocating materials on the site and any type of noise

Maret Athletics Field Page 2 of 9 MCN BUILD INC.



- Please direct all complaints, questions, or concerns to the question/complaint form
- Contact: Johnny Seikaly johnny.seikaly@mcnbuild.com; (202) 333-3424

Maret Athletics Field Page 3 of 9 MCN BUILD INC.



II. Project Photographs

Figures 1 – 3: Permit and Signage Boards



Maret Athletics Field Page 4 of 9 MCN BUILD INC.







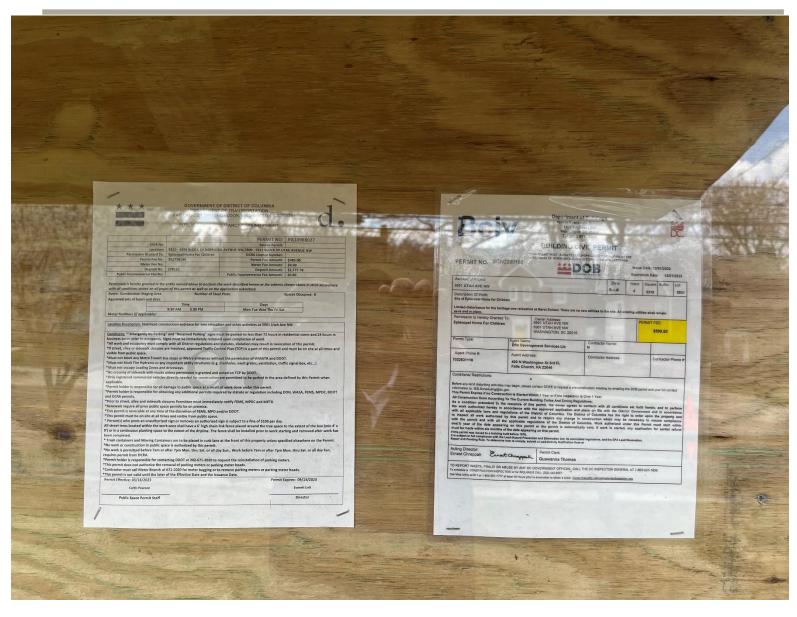




Figure 4: Heritage #1 move completed



Figure 5: Heritage #2 move completed

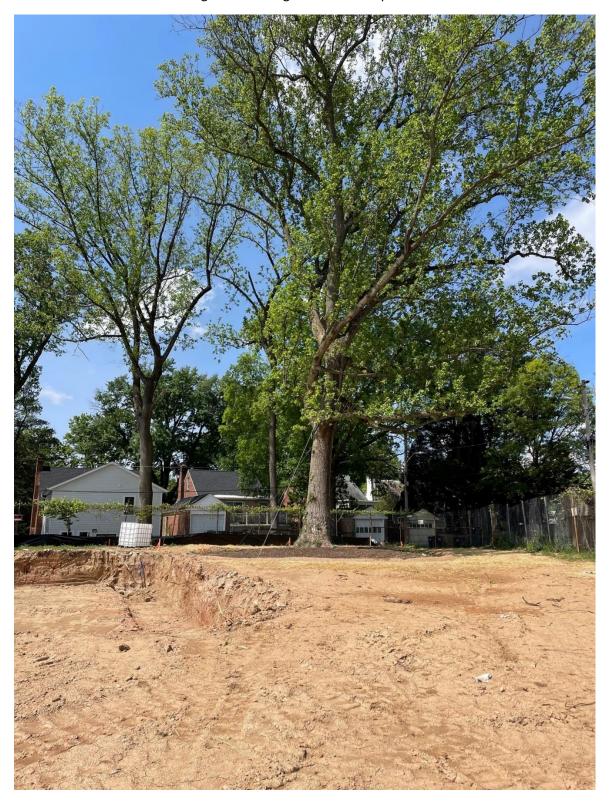




Figure 6: Heritage #3 move in progress

